



Photo 9: Similar view to previous.



Photo 11: Verandah roof on (temporary) ward #6. All timbers are nailed. No hurricane clips or other fixings are present.



Photo 10: Close up of temporary facilities. There are no positive fixings holding the superstructure to the foundations.

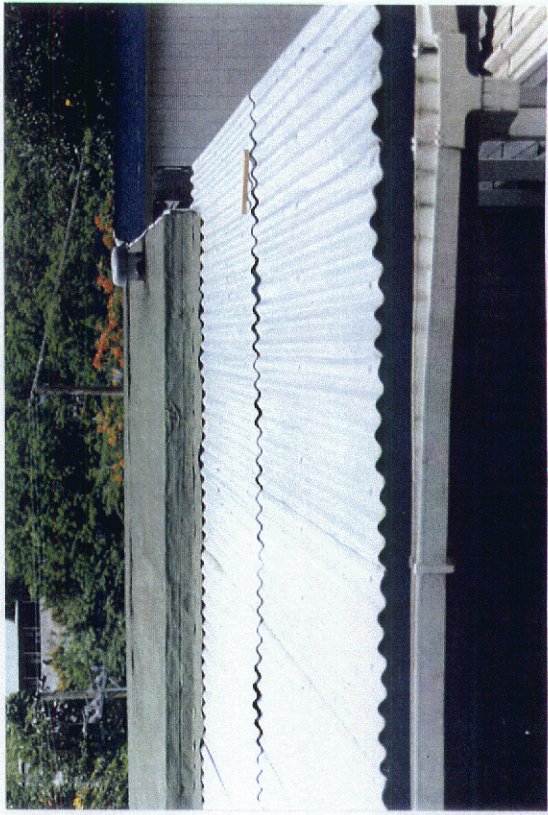


Photo 12: View of roof of temporary buildings. Drive screws are placed at 9" to 12" centres throughout over the verandah.
